


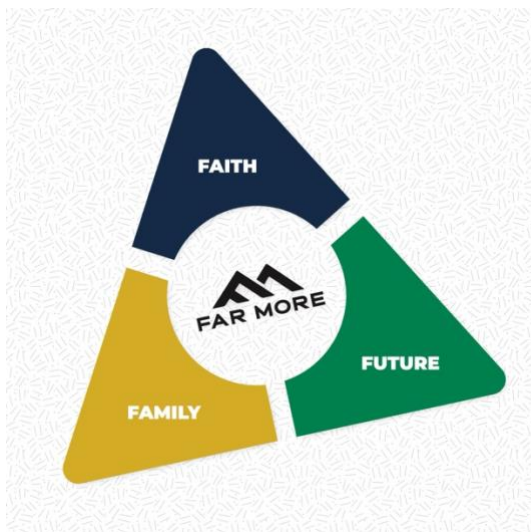

## **“BEHIND THE PLYWOOD”**

### **Far More Vision REMODEL Update October 1, 2025**

In the three weeks since our last update, hundreds of kids and their families have moved into our children’s ministries spaces. They LOVE it! A few final pieces in phase 1 are arriving soon (classroom doors, operable walls in Family Lobby and rooms 110/111, restroom sinks). If you missed the last phase 1 update, check it out [HERE](#).

Phase 2 has started quickly:


- Demo 95% complete – last precast wall into existing Lobby coming down soon
- New walls for entries, offices, storage, restroom nearly complete
- Exterior mansard removed preparing for new insulated EIFS walls
- Elevator opening into building open and pit ready for foundations

Yes...all of this done in 3 weeks! Amazing progress.

*Now to him, who is able to do **FAR MORE** abundantly than all that we ask or think, according to the power at work within us, to him be glory in the church and in Christ Jesus throughout all generations, forever and ever. Amen. [Eph.3:20-21]*



Beginning of opening from Lobby to new North Hallway/Entrance

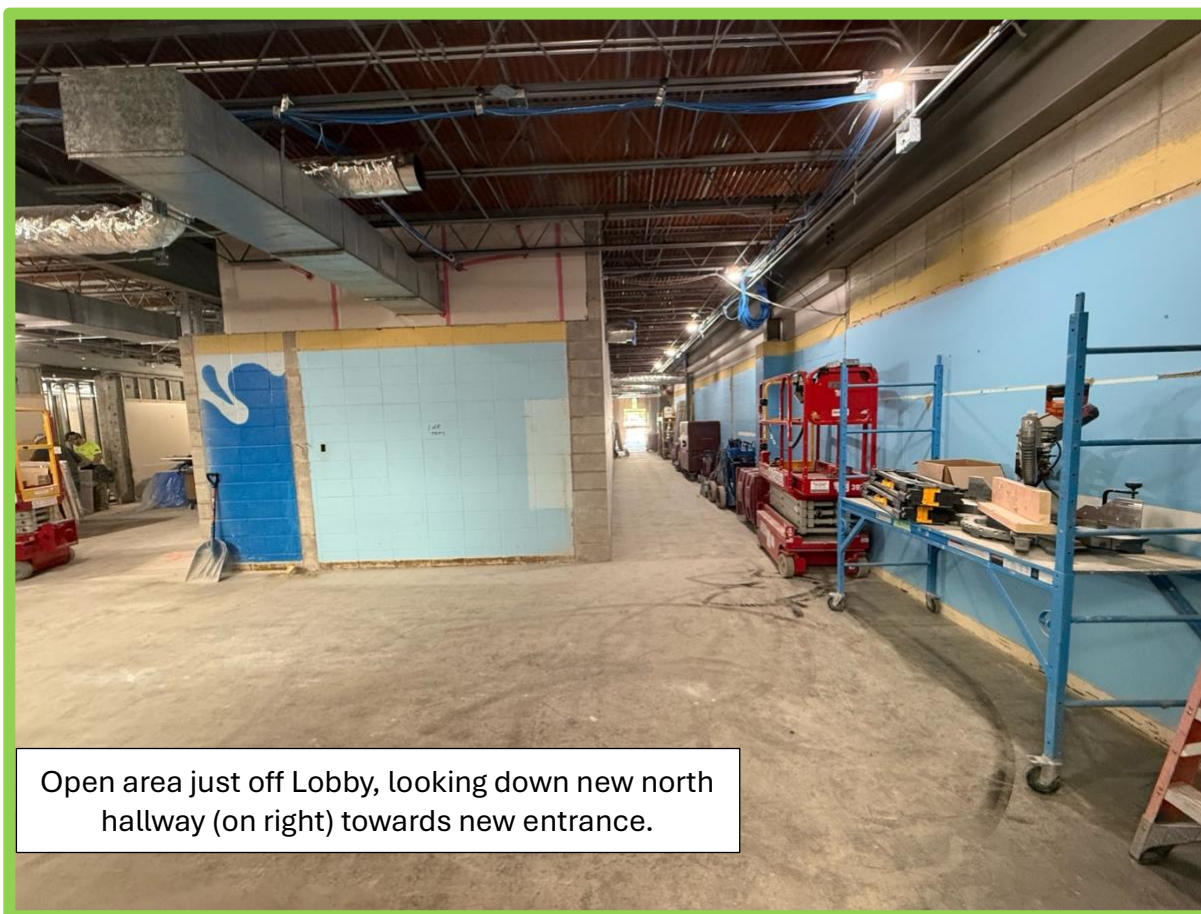

Open area just off Lobby, looking down new north hallway (on right) towards new entrance.



Pit for elevator ready for foundation. Opening in building with new North Entry on left, elevator on right,
